


SW - Judith A. Resnik Middle School

August 13, 2015

Southwest ISD
Subcommittee Report 09

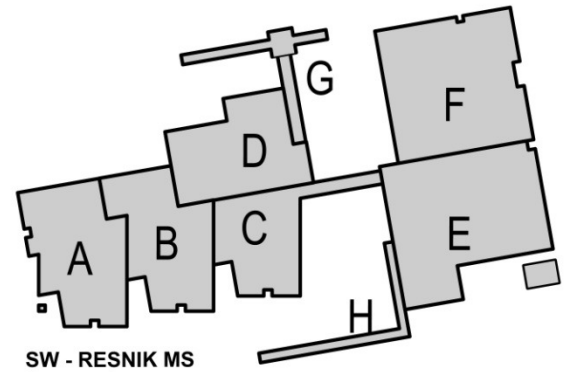

PROJECT SUMMARY:

General Contractor: Joeris General Contractors, LTD.

Notice to Proceed: October 20, 2014
Substantial Completion Date: July 18, 2016

Original Guaranteed Maximum Price (GMP): \$110,500,000.00
Current Guaranteed Maximum Price (GMP): \$111,000,000.00

Judith A. Resnik Middle School: \$27,174,390.00

Change Orders to Date: 1

Percentage of Completion as of 7/31/15: MS Package (#9) - 44%

Current Work:

Middle School:

1. Rough grading & backfilling continues at Site/Field areas adjacent to MS building.
2. Driveway curbs have been poured, backfilling in progress.
3. Structural steel roof decking in progress at Areas A & B.
4. Major Concrete Pours are complete for 1st Flr. & 2nd Flr.
5. MEP rough-in in Areas C, D, E & F continue. Masonry walls in Area E & F are complete.
6. Interior Stud/Gypsum Bd. installation work in Areas E & F continue. Area C & D in Progress (1st Flr.)
7. Exterior Insulation work in progress at Area D. Masonry Stone/Brick work in progress Area D, E & F.
8. Roof work continues at High Roof Area E & F. Area C & D have commenced.





SW MS – Ext. Sheathing/Window work at Area C.



SW MS – Material Storage – H.M. Frames.



SW MS – First Floor Concrete Pour at Area A



SW MS – Brick Work - Area E
