


## SW - Judith A. Resnik Middle School

September 10, 2015

Southwest ISD  
Subcommittee Report 10

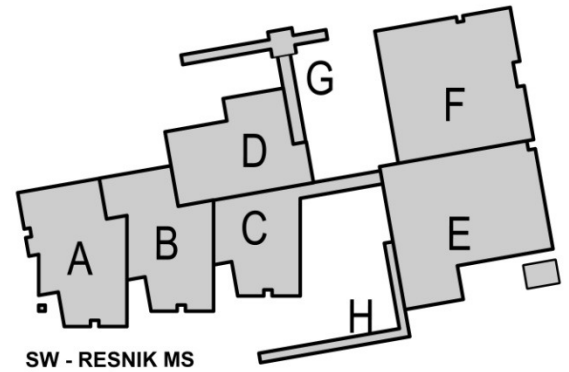

### PROJECT SUMMARY:

**General Contractor:** Joeris General Contractors, LTD.

**Notice to Proceed:** October 20, 2014

**Substantial Completion Date:** July 18, 2016

**Original Guaranteed Maximum Price (GMP):** \$110,500,000.00

**Current Guaranteed Maximum Price (GMP):** \$111,000,000.00

**Judith A. Resnik Middle School:** \$27,174,390.00

**Change Orders to Date:** 1

**Percentage of Completion as of 8/31/15:** MS Package (#10) - 57%

### Current Work:

#### **Middle School:**

1. Rough grading & backfilling continues at Site/Field areas adjacent to MS building.
2. Irrigation lines in progress at MS Athletic Fields.
3. Driveway curbs have been poured, sidewalks & misc. flatwork in progress.
4. Major structural steel & concrete Work is complete.
5. Interior stud/gypsum bd. installation work in Areas C & D continue.
6. Metal stud installation in progress in areas B & C second floor.
7. Ext. Insul. work in progress at Area A & B. Masonry Stone/Brick work in progress Area C & D.
8. Roof work continues at high roof Area A & B. Building dried-in.
9. Mechanical unit installation in progress in Area E & F roofs. MEP rough-in on-going in all areas.
10. Exterior Canopies in progress at Areas G & H.



SW MS – Exterior Insulation/Brick Masonry Installation – View towards Areas A, B & C




SW MS – Ext. Brick/Insulation work at Area C.



SW MS – AC Unit Installation at Area F Roof.



SW MS – Interior Work at Competition Gym - Area F

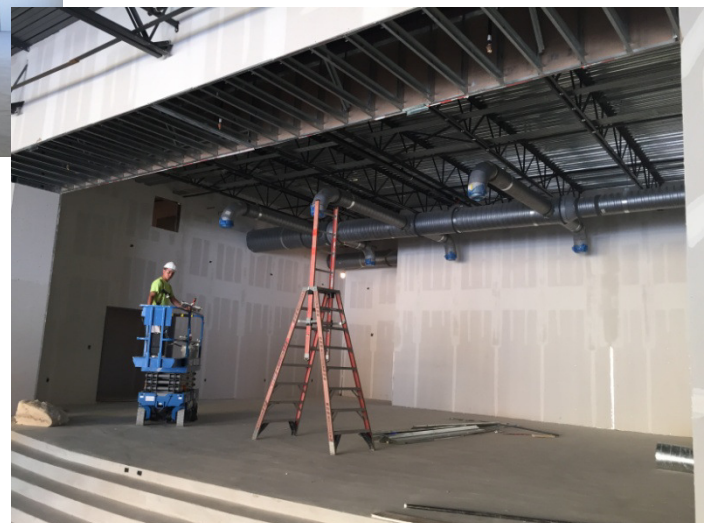

SW MS – Interior Work at Cafeteria Stage- Area E
